

# PROJECT STATUS REPORT

March 2018 ♦ Issue 27



SAN LUIS OBISPO COUNTY COMMUNITY COLLEGE DISTRICT

## North County Campus Center

---

### Project Overview

The new Cuesta College North County Campus Center Building will be a 43,000 square foot, two-story structure. It will house the various programs and offices displaced by the removal of non-compliant modular buildings. The demolition of these modular buildings has been completed in preparation for the new Campus Center Building. The project delivery method is CM Multi-Prime and contains thirteen trade bid packages.

### Project Progress

At the beginning of March, the main entry curtainwall installation was completed along with the tile for the main lobby staircase and handrails. The first and second floor offices, first floor classrooms and around the computer lobby area have all received carpet. Ceiling tiles have been installed in many of the rooms and all the linear metal ceiling panels are up. The fire sprinkler system is 99% complete and will wrap up by the end of the month. Site concrete is ongoing and is also on track for completion by the end of March. Casework was delivered at the beginning of the month and has been installed in their respective rooms, countertops will be installed next month.

### Project Schedule


As the project is nearing completion, the contractors are finishing up their remaining items. Items such as finishing ceiling tile and carpet in the remaining rooms, countertops and plumbing finishes. The kitchen floor tile has begun installation and kitchen equipment will follow. The building's furniture is scheduled for delivery into the building in April with installation beginning on the second floor.



Main Entry Progress



Interior Stair Handrail

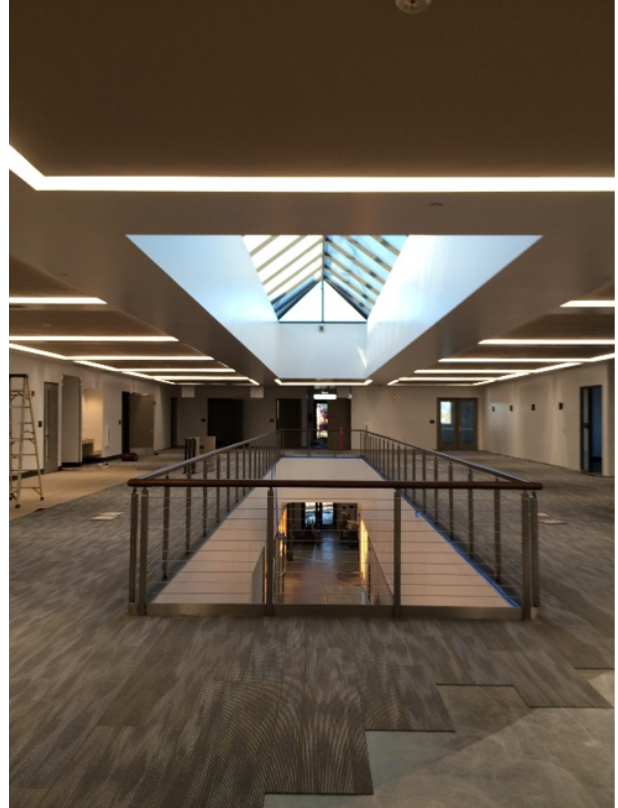

Open Computer Lab Progress



First Floor Drinking Fountain



First Floor Workroom Casework
