

PROJECT STATUS REPORT

September 2022 ♦ Issue 81

SLO Campus 5200/6100 Switchgear Replacement

Project Overview

The SLO Campus 5200/6100 Switchgear Replacement project consists of replacing the existing switchgear to provide electrical provisions to the 5000 and 6000 complex buildings. The 6000 complex will also receive a new switchgear enclosure structure that will land on the west side of Building 6300. The project was bid on June 21, 2022 and awarded to Newton Construction & Management on July 7, 2022. Construction started in early August and is planned to be completed by the end of the year.

Project Progress

In the month of September, the contractor completed the utility replacement and began over-excavation and compaction of the new enclosure pad. Earthwork for duct bank installation and footing forms is in progress.

Project Schedule

In the upcoming month, the contractor will pour the footings for the new switchgear enclosure and begin erection of the slump stone masonry walls.



New Sewer Line



Finished Building Pad

**SLO Campus
4k-6k Restroom & Drinking
Fountain ADA Upgrades**

Project Overview

The SLO Campus 4000-6000 Restroom & Drinking Fountain ADA Upgrades project consists of demolishing and reconstructing existing restrooms and drinking fountains in buildings 4100, 4200, 4300, 4600, 5100, 5400, 6100, and 6200. The project was bid on June 16, 2022 and awarded to Newton Construction & Management on July 7, 2022. Construction started in early August and is planned to be completed by the end of the year.

Project Progress


In the month of September, the contractor completed demolition in 5100 and underground plumbing has commenced in buildings 4100 and 6100. Concrete patch back is complete in buildings 4200 and 4600 and framing is in progress.

Project Schedule

In the upcoming month, the contractor will continue framing and reconstruction of the 4200 and 4600 restrooms and complete the plumbing installation in the 4100 and 6100 Restrooms. Phase 2 restrooms of 4300 and 6200 will begin 11/1.



4200 Framing

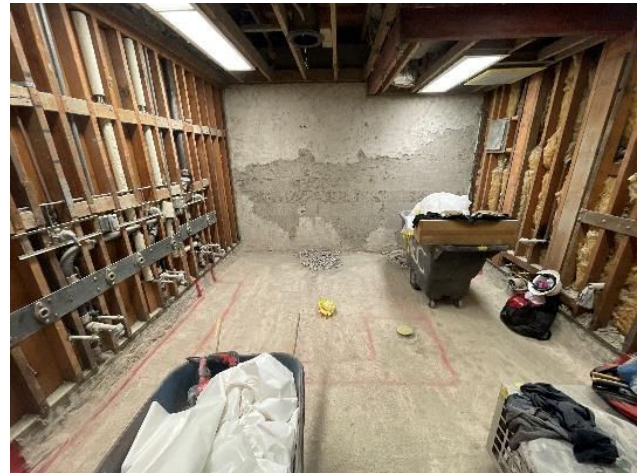

6100 Plumbing Layout

**SLO Campus
CoE Fiber Run**

Project Overview

The SLO Campus County of Education Fiber Run project consists of new underground conduit and fiber optic cable to provide a revamped connection between the data center on the Cuesta campus and the CoE office. The project also includes a section of new underground conduit in front of building 6600 to provide future pathway. The project was bid on February 17, 2022 and awarded to Taft Electric on March 3, 2022. Construction started in mid-July and is planned to be completed by October 2022.

Project Progress

In the month of September, the contractor completed all boring, underground conduit, and vault installation on the CoE property.

Project Schedule

The specified fiber is out of stock and a substitution needs to be identified to complete the project.



Conduit Trench to CoE Mediaplex



New Vault on CoE Property
