

# PROJECT STATUS REPORT

March 2023 ♦ Issue 87

## SLO Campus 4k-6k Restroom & Drinking Fountain ADA Upgrades

---

### Project Overview

The SLO Campus 4000-6000 Restroom & Drinking Fountain ADA Upgrades project consists of demolishing and reconstructing existing restrooms and drinking fountains in buildings 4100, 4200, 4300, 4600, 5100, 5400, 6100, and 6200. The project was bid on June 16, 2022 and awarded to Newton Construction & Management on July 7, 2022. Construction started in early August and is planned to be completed by the end of April 2023.

### Project Progress

In the month of March, the contractor completed and opened the restrooms at Buildings 4100, 4200, 4300, 4600, 5100, and 6100. The construction in Building 6200 is ongoing.

### Project Schedule

In the upcoming month, the contractor will continue framing and fixture installation in Building 6200. The project is scheduled to be completed by the end of April.




5100 men's restroom



5100 women's restroom



5100 women's restroom

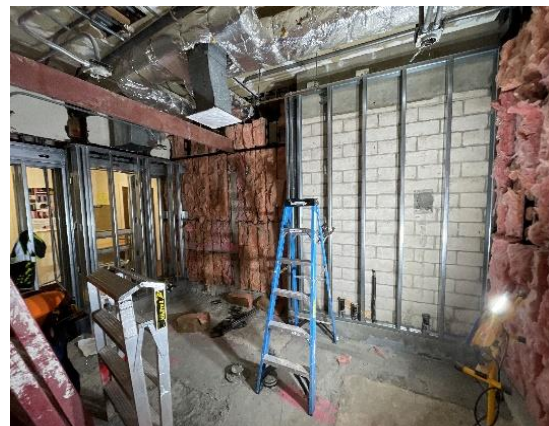

6200 women's restroom

---

# PROJECT STATUS REPORT

March 2023 ♦ Issue 87

## SLO Campus 5200/6100 Switchgear Replacement

---

### Project Overview

The SLO Campus 5200/6100 Switchgear Replacement project consists of replacing the existing switchgear to provide electrical provisions to the 5000 and 6000 complex buildings. The 6000 Complex will also receive a new switchgear enclosure structure that will land on the west side of Building 6300. The project was bid on June 21, 2022 and awarded to Newton Construction & Management on July 7, 2022. Construction started in early August and is planned to be completed by the end of April 2023.

### Project Progress

In the month of March, the contractor completed the masonry structure, roof framing, and concrete ramp. The first coat of plaster is in process and pieces of equipment are beginning to arrive onsite.

### Project Schedule

In the upcoming month, the contractor will continue with exterior finish and door installation. Fencing will be removed once construction is complete. The switchgear will be installed during winter break.



roofing underlayment



roof framing



duct work



temporary transformer

---



# PROJECT STATUS REPORT

March 2023 ♦ Issue 87

## SLO Campus CoE Fiber Run

### Project Overview

The SLO Campus County of Education Fiber Run project consists of new underground conduit and fiber optic cable to provide a revamped connection between the data center on the Cuesta campus and the CoE office. The project also includes a section of new underground conduit in front of building 6600 to provide future pathway. The project was bid on February 17, 2022 and awarded to Taft Electric on March 3, 2022. Construction started in July 2022 and is planned to be completed by April 2023.

### Project Progress

In the month of March, the contractor continued to work on punch list and site observation items. Final punch walk is scheduled for 3/30/23.

### Project Schedule

Project schedule will be updated once punch list has been completed and contractor is authorized to proceed with demolition scope.



duct sealer in vaults



spare conduit labeling



fiberoptic labeling in vaults



fiberoptic labeling in vaults
