

PROJECT STATUS REPORT

October 2023 ♦ Issue 94



SAN LUIS OBISPO COUNTY COMMUNITY COLLEGE DISTRICT

SLO Directory Wayfinding & Signage

Project Overview

The SLO Directory Wayfinding & Signage project consists of the installation of new pedestrian directional signs atop concrete bases. The directories at the perimeter of the campus will have power run to them for internal illumination, while the intercampus wayfinding signs will be collocated with light poles for easy viewing. The project was bid on May 11, 2023 and awarded to Ellis & Ellis Sign Systems on June 7, 2023. Construction started on October 16, 2023 and is planned to be completed by December 1, 2023.

Project Progress


In the month of October, the contractor completed the demolition of the old signage structures and dug footings for the new directories.

Project Schedule

In the upcoming month, the contractor will proceed with select saw-cutting, electrical installation, concrete pouring, and sign placement. The anticipated completion date for this project is November 3, 2023.



Covered Display to be Demolished

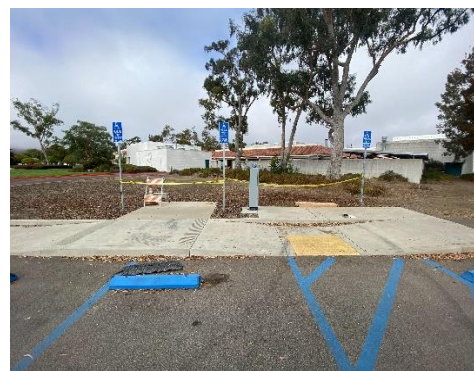

Covered Display Post-Demo



Directory Signage Footing



Covered Footing Location

PROJECT STATUS REPORT

October 2023 ♦ Issue 94

SLO Campus Center

Project Overview

The SLO Campus Center project consists of a new 33,728 SF, two-story building that replaces the existing Administration Building 8000. The scope of the new building includes offices, student services, a boardroom, a cafe, and meeting and break rooms. Sitework includes underground utilities, driveways, fire and maintenance access roads, parking lots, a new bus stop location, concrete paths, and planting and irrigation. The entire site is roughly five acres large. The project was bid on February 9, 2023 and awarded to Wysong Construction on April 5, 2023. Construction started in early May and is planned to be completed by Summer 2025.

Project Progress

In the month of October, the contractor completed the concrete perimeter curb and slab-on-grade on the east 1/3 of the structure. The remaining 2/3 is being formed for upcoming concrete pours.

Project Schedule

In the upcoming month, the contractor will continue to form and pour the building slab-on-grade while steel material identification commences. The project remains on schedule.



East 1/3 Slab-on-Grade Pour



East 1/3 Slab-on-Grade Pour



Perimeter Curbs



East 1/3 Slab-on-Grade Concrete
