



**CONSTRUCTION UPDATES & ACTIVITIES**


*Week Ending November 3, 2023*

**SLO Campus Center**

**Work this week:** The contractor continues forming perimeter footing and wall form boards on the west 1/3 of the building. Under slab vapor barrier & slab on grade rebar was installed on the west 1/3 of the building. Slab concrete was placed on a portion of the west 1/3 of the building.

Site utility contractor was not onsite this week.

- Noise:** Loud noise from equipment & trucking
- Parking:** No Impacts
- Utilities:** No Impacts
- Odors:** None

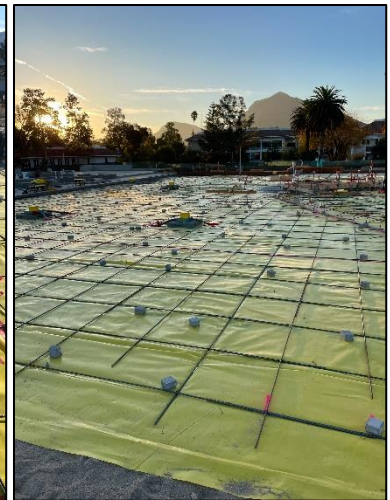

*Under Slab Vapor Barrier & Rebar (West Side)*



*Electrical Rm. Wall Curb Forms*



*Restroom Slab & Curb (West Side)*



*Slab Pour (West Side)*
