

SLO Building 7300 Telecom Room Upgrade

Project Overview

The SLO Building 7300 Telecom Room Upgrade Signage & Wayfinding (DSA) project consists of separating the network cabling from the AV cabling, testing, relabeling, and installing a new two-post rack and network cabinet. The project was awarded to Thoma Electric on January 4, 2024. Construction started on February 5, 2024, and is scheduled to be completed by February 23, 2024.

Project Progress

In the month of February, the contractor tested and reorganized the cables in the telecom room closet. The new two-post rack and AV cabinet were also installed. Only labeling remains to be completed.

Project Schedule

The project will be completed by February 23, 2024.




Original TR Closet Configuration



New TR Closet Configuration



New Network Cabinet

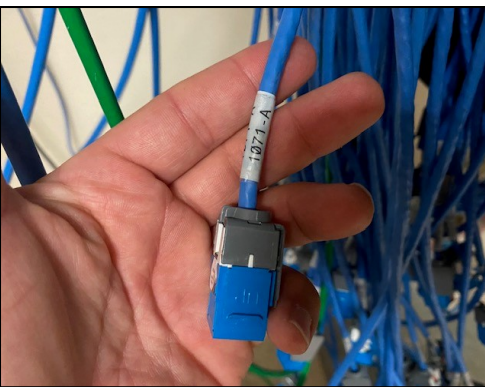

New Data Port Connectors

SLO Building Signage & Wayfinding (DSA)

Project Overview

The SLO Building Signage & Wayfinding (DSA) project consists of the fabrication and installation of new campus identification building numbers, street name signs, parking permit signs, and Cuesta College branding wall signs. Some electrical and concrete patching is also included in the scope. The project was bid on May 11, 2023 and awarded to A Good Sign & Graphis Company on June 7, 2023. Construction started on January 2, 2024 and is scheduled to be completed by March 29, 2024.

Project Progress

In the month of February, the contractor completed the installation of new building number signage on the 1000, 2000, 3000, and 4000 Complexes.

Project Schedule

In the upcoming month, the contractor will continue the ID signage installation at the 5000, 6000, and 7000 Complexes.



Building 1000 Installation



Building 1400 Installation



Building 7100 Installation



Building 5100 Demo

Project Overview

The SLO Campus Center project consists of a new 33,728 SF, two-story building that replaces the existing Administration Building 8000. The scope of the new building includes offices, student services, a boardroom, a cafe, and meeting and break rooms. Sitework includes underground utilities, driveways, fire and maintenance access roads, parking lots, a new bus stop location, concrete paths, and planting and irrigation. The entire site is roughly five acres large. The project was bid on February 9, 2023 and awarded to Wysong Construction on April 5, 2023. Construction started in early May and is planned to be completed by Summer 2025.

Project Progress

In the month of February, the contractor continued to erect the structural steel and began installing the 2nd floor metal decking. Additionally, work on the parking lot 3 expansion continued with curb, gutter, and sidewalk forming and concrete pours.

Project Schedule

In the upcoming month, the contractor will finish the structural steel erection and metal decking while continuing to progress on the site improvements. The project remains on schedule per the critical path.



Setting Signed Beam



Structural Steel Erection



2nd Floor Metal Decking



Grade New Sidewalk – Lot 3
