



CONSTRUCTION UPDATES & ACTIVITIES

Week Ending May 10th, 2024

SLO 5000 Roof & HVAC Replacement

Work this week:

- Contractor site survey and site safe off
- Temp air installed for 5400 meeting room
- Contractor disconnect and disassembly of 5400 HVAC
- Contractor lay down area secured and fenced – dock area 5200
- HVAC equipment demo 5400 roof – crane operations
- Roof material demo 5400

Noise: Loud noise from equipment and demolition activities
Parking: Entire parking lot area behind 5100 (bookstore) secured
 Heavy equipment parking area moved to dirt lot adjacent to 5100 dock
Utilities: Main electrical breaker for 5400 HVAC power supply closed and locked out
 Gas feed for 5400 roof turned off at 5100 roof
Odors: None



Laydown




HVAC Disconnect



Crane Demo



Temp Air

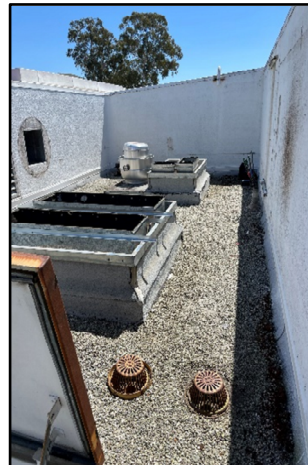

HVAC Removed



Roof Demo
