



CONSTRUCTION UPDATES & ACTIVITIES

Week Ending May 17th, 2024

SLO 5000 Roof & HVAC Replacement

Work this week:

- Complete roof demo for 5400 upper and lower roofs
- Temp air installed in 5100 offices and dining room
- Drains scoped and video recorded
- Roof drains replaced 5400 upper and lower roofs
- New roof completed for 5400 upper and lower
- Demo of gravel commenced for remainder of building
- Parapet caps on 2 week backorder delay

Noise:	Loud noise from equipment and demolition activities
Parking:	Entire parking lot area behind 5100 (bookstore) secured
Utilities:	Main electrical breaker for 5400 HVAC power supply closed and locked out Gas feed for 5400 roof turned off at 5100 roof
Odors:	None



Forklift Operations



Gravel Demo 5100




5400 Drain Replacement



5400 Upper Roof Demo



5400 Lower New Roof

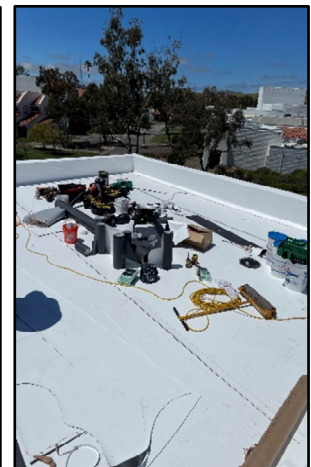

5400 Upper New Roof
