



CONSTRUCTION UPDATES & ACTIVITIES


Week Ending June 14th, 2024

SLO 5000 Complex


Work this week:

- Electrical and gas safe off 5200/5300
- All HVAC equipment disconnected ready for demo 5200/5300
- All roofing material demolished and removed 5200/5300
- Roof drains completed 5200 and 5300
- 1 sheet plywood replaced 5200/5300
- Temp air installed 5200/5300
- Single ply roof material completed 5100
- New HVAC equipment craned onto 5100

- Noise:** Loud noise from equipment and demolition activities.
- Parking:** Entire parking lot area behind 5100 (bookstore) secured.
- Utilities:** Main electrical breaker for 5100, 5200, 5300 and 5400 HVAC power supply closed and locked out. Gas feed for 5100, 5200, 5300 and 5400 roofs turned off.
- Odors:** None

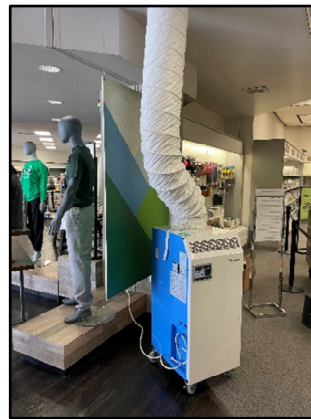


Temp Air 5200

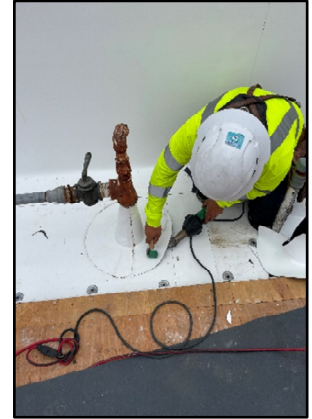

Welding Single Ply



Roof Demo 5300/5200

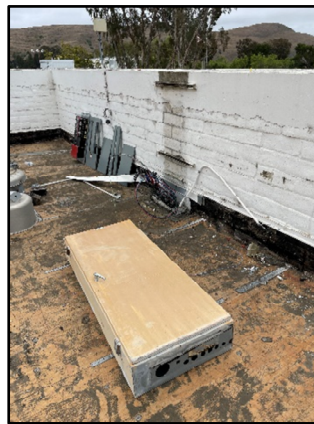

Safe Off 5200/5300



New Platform Cap 5100
